

Quality Control

TILED DECK QC SHEET

Project Name: _____

Subcontractor: _____


Area Covered by QC sheet: _____

Fax Number: _____

Gripset 38 / Gripset 2P membrane Installation item	Comply (Y/N)	Sign-off (Initials)	Comments
Concrete clean, smooth and dry. Soft porous concrete diamond ground, all dust and debris removed.			
All cracks and construction joints flashed with RF or Gripset elastofabric tapes to specification.			
All concrete repairs undertaken with Gripset C-Plug concrete repair mortar.			
Fibre cement board stagger-laid with each sheet off-set at least 300mm edges supported 400mm maximum span.			
Screw/Glue fixed to specifications. No loose or drummy sheets. 5mm gap to all abutments.			
Drains outlets and overflows recessed and installed to specification.			
All sheet joints flashed with RF or Gripset elastofabric tapes to specifications.			
All non-standard details installed as per pre-approved specification (attach approved drawings).			
Movement joints identified and installed to approved specification detail (attach approved detail).			
Weather conditions suitable for laying.			
Gripset SB MS sealant applied to outlet fitting.			
Substrate primed to specification with good coverage and penetration.			
Elastofabric installed to all movement joints, internal and external corners.			
Fibre Cement Boards joints flashed and reinforced with RF Fabric tapes or butylFLASH™ P tapes.			
All penetrations completed to specification including under/over flashing.			
Gripset 38 or 2P applied to specification to the minimum dry film thickness required.			
Total coat weight to specification (minimum dry film thickness 1.5mm) Check actual volume versus estimate.			
Overall installation free of wrinkles, bubbles, bridging, splits or lumps.			
Any mechanical damage to membrane repaired to specification.			
Paver pedestals, timber raft or Schluter Ditra system will be installed over Gripset 38 or 2P before laying tiles onto membrane.			
Laticrete 4XLT adhesive applied to specification and good trade practice at the required coverage for the Schluter Ditra system.			
Job sheets completed recording area installed, date of installation and batch numbers.			

TILED DECK QC SHEET

Membrane Coverage Calculation:

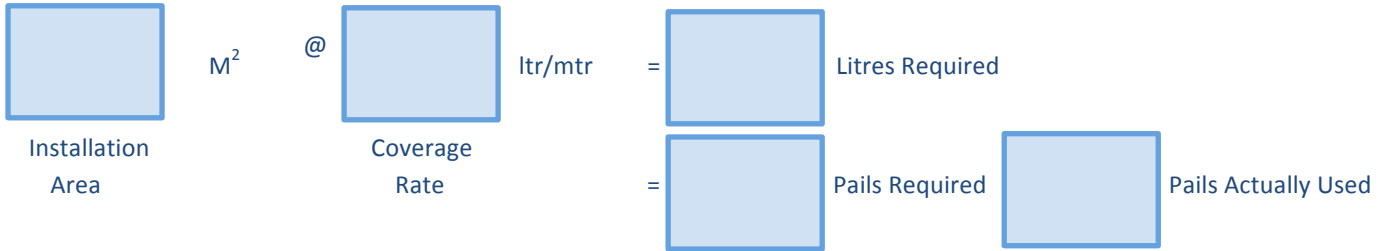

Reinforcements Used:

butylFLASH P	RF Fabric Tapes
Elastofabric	Chopped Strand Fibre

Issues to note or raised during installation:

Remedial Action Required:

Note of damaged areas repaired:

Attach any photographs taken during application.
