

Quality Control



TILED INTERNAL WET AREA QC SHEET

Project Name: _____

Subcontractor: _____


Area Covered by QC sheet: _____

Fax Number: _____

Gripset 38 / Gripset 2P membrane Installation item	Comply (Y/N)	Sign-off (Initials)	Comments
Concrete clean, smooth and dry. Soft porous concrete diamond ground, all dust and debris removed			
All cracks and construction joints flashed with Gripset elastofabric tapes to specification.			
All concrete repairs undertaken with concrete repair mortar.			
Flooring overlaid with Hardies Tile-to-Timber, tight butted and staggered. Sheets offset to plywood sheets.			
Hardies sheets screw fixed to specification. No loose or drummy sheets.			
Drains and outlets recessed and installed to specification.			
All sheet joints flashed with RF or butylFLASH tapes to specification.			
All non-standard details installed as per pre-approved specification (attach approved drawings).			
Substrate primed to specification with good coverage and penetration.			
Gripset elastofabric tapes installed at all junctions.			
Gripset elastofabric internal and external corners have been fitted.			
All up stands, corners and substrate sheet joints flashed and reinforced with RF or butylFLASH Fabric tapes.			
Gripset SB MS sealant applied to outlet fitting.			
Movement joints identified and installed to approved specification/detail (attach approved detail).			
All penetrations completed to specification including under/over flashing.			
Wall membrane installed to specification at least 2m high with corners reinforced with RF Fabric tapes or butylFLASH™ P			
Total coat weight to specification (min. dry film thickness 1.2mm). Check actual volume used versus estimate.			
Gripset 38 or 2P applied to specification to the minimum dry film thickness required.			
Overall installation free of wrinkles, bubbles, bridging, splits or lumps.			
Any mechanical damage to membrane repaired to specification.			
Paver pedestals, timber raft or Schluter Ditra system will be installed over Gripset 38 or 2P before laying tiles onto membrane.			
Laticrete 4XLT adhesive applied to specification and good trade practice at the required coverage for the Schluter Ditra system.			
Job sheets completed recording area installed, date of installation and material batch numbers used.			

TILED INTERNAL WET AREA QC SHEET

Membrane Coverage Calculation:

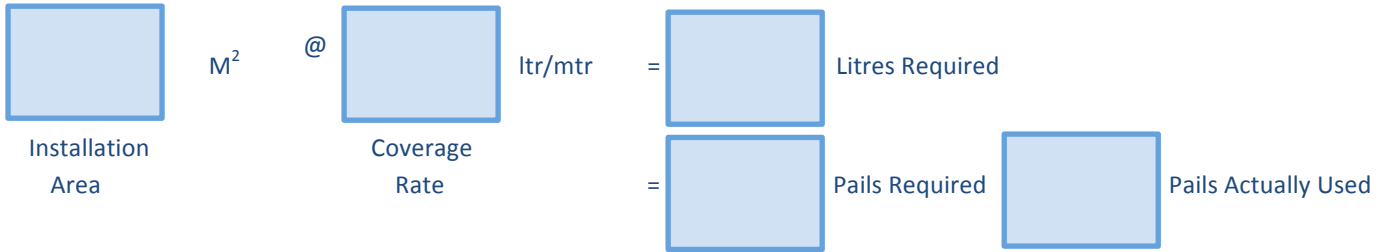

Reinforcements Used:

butylFLASH P RF Fabric Tapes
Elastofabric Chopped Strand Fibre

Issues to note or raised during installation:

Remedial Action Required:

Note of damaged areas repaired:

Attach any photographs taken during application.
